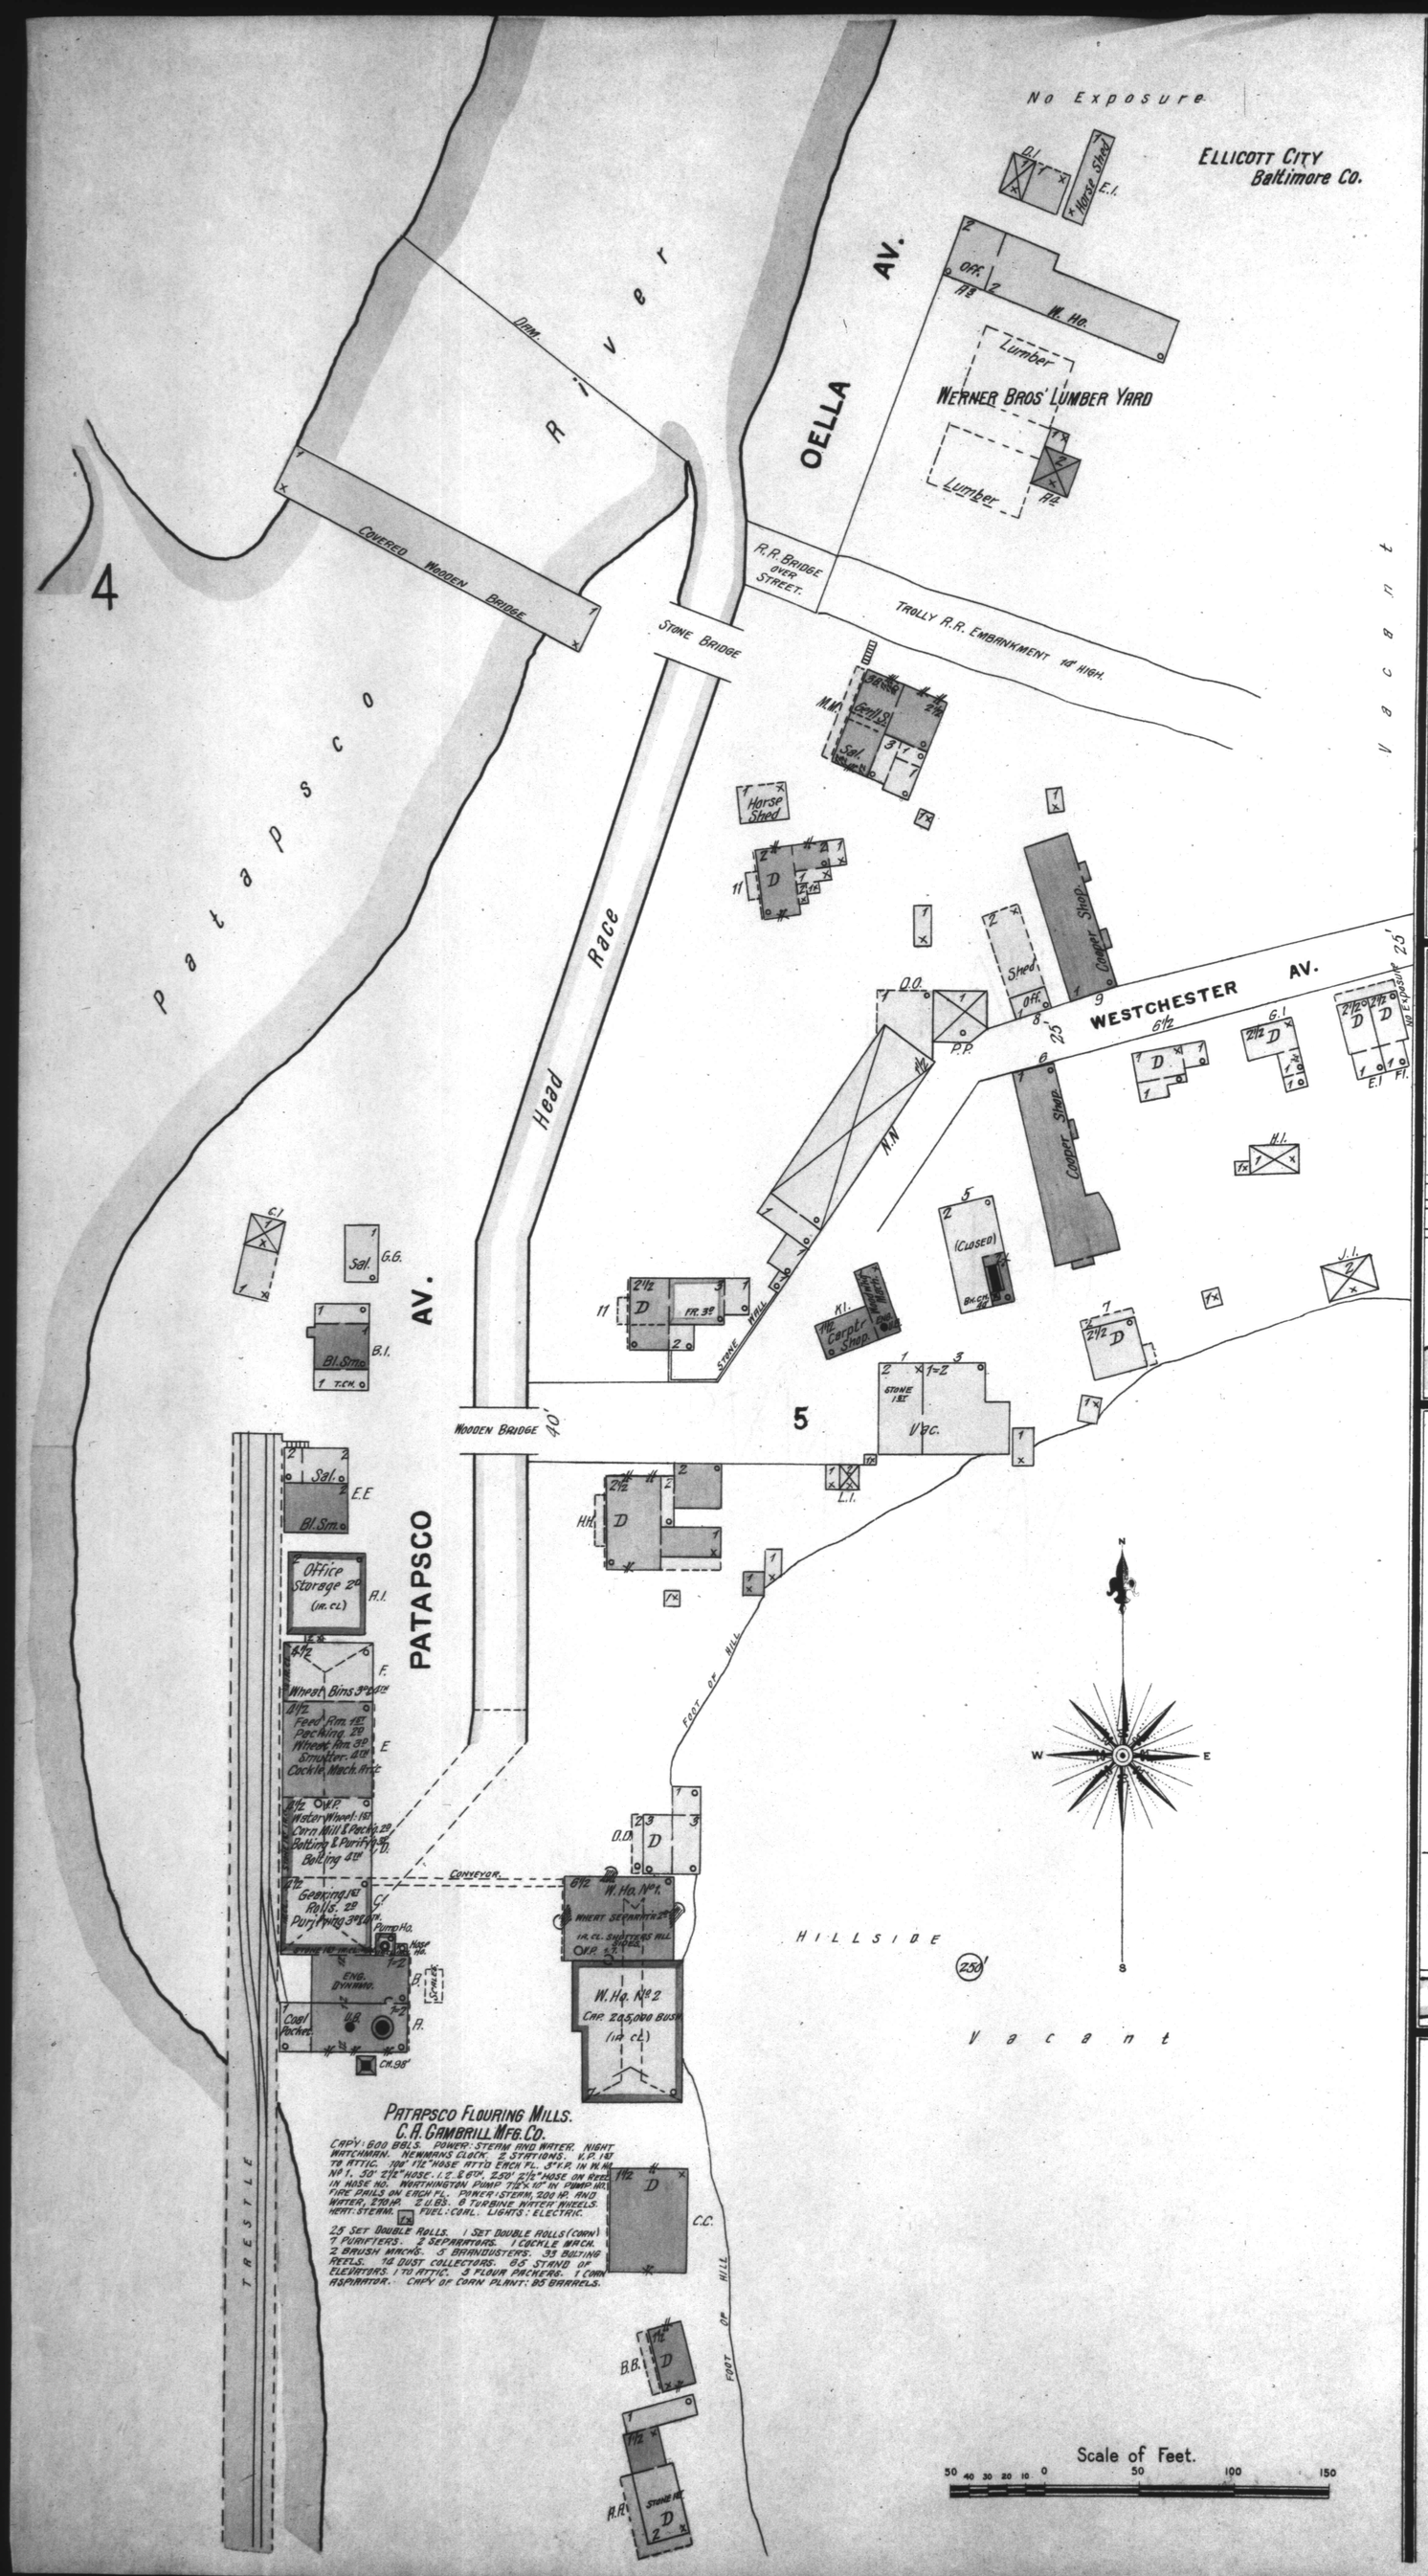

PATAPSCO FLOURING MILLS.
C. H. GAMBRILL MFG. CO.

CAPY: 600 BBLS. POWER: STEAM AND WATER. NIGHT WATCHMAN. NEWMANS CLOCK. 2 STATIONS. V.F. 1ST TO ATTIC. 100' 1½" HOSE ATTD EACH FL. 3rd F.P. IN W. HO. No 1. 50' 2½" HOSE. 1.2. & 6th. 2.50' 2½" HOSE ON REEL IN HOSE HO. WORTHINGTON PUMP 7½" x 10" IN PUMP HO. FIRE PAILS ON EACH FL. POWER: STEAM. 200 HP. AND WATER, 270 HP. 2 U.BS. 6 TURBINE WATER WHEELS. HEAT: STEAM. FUEL: COAL. LIGHTS: ELECTRIC.
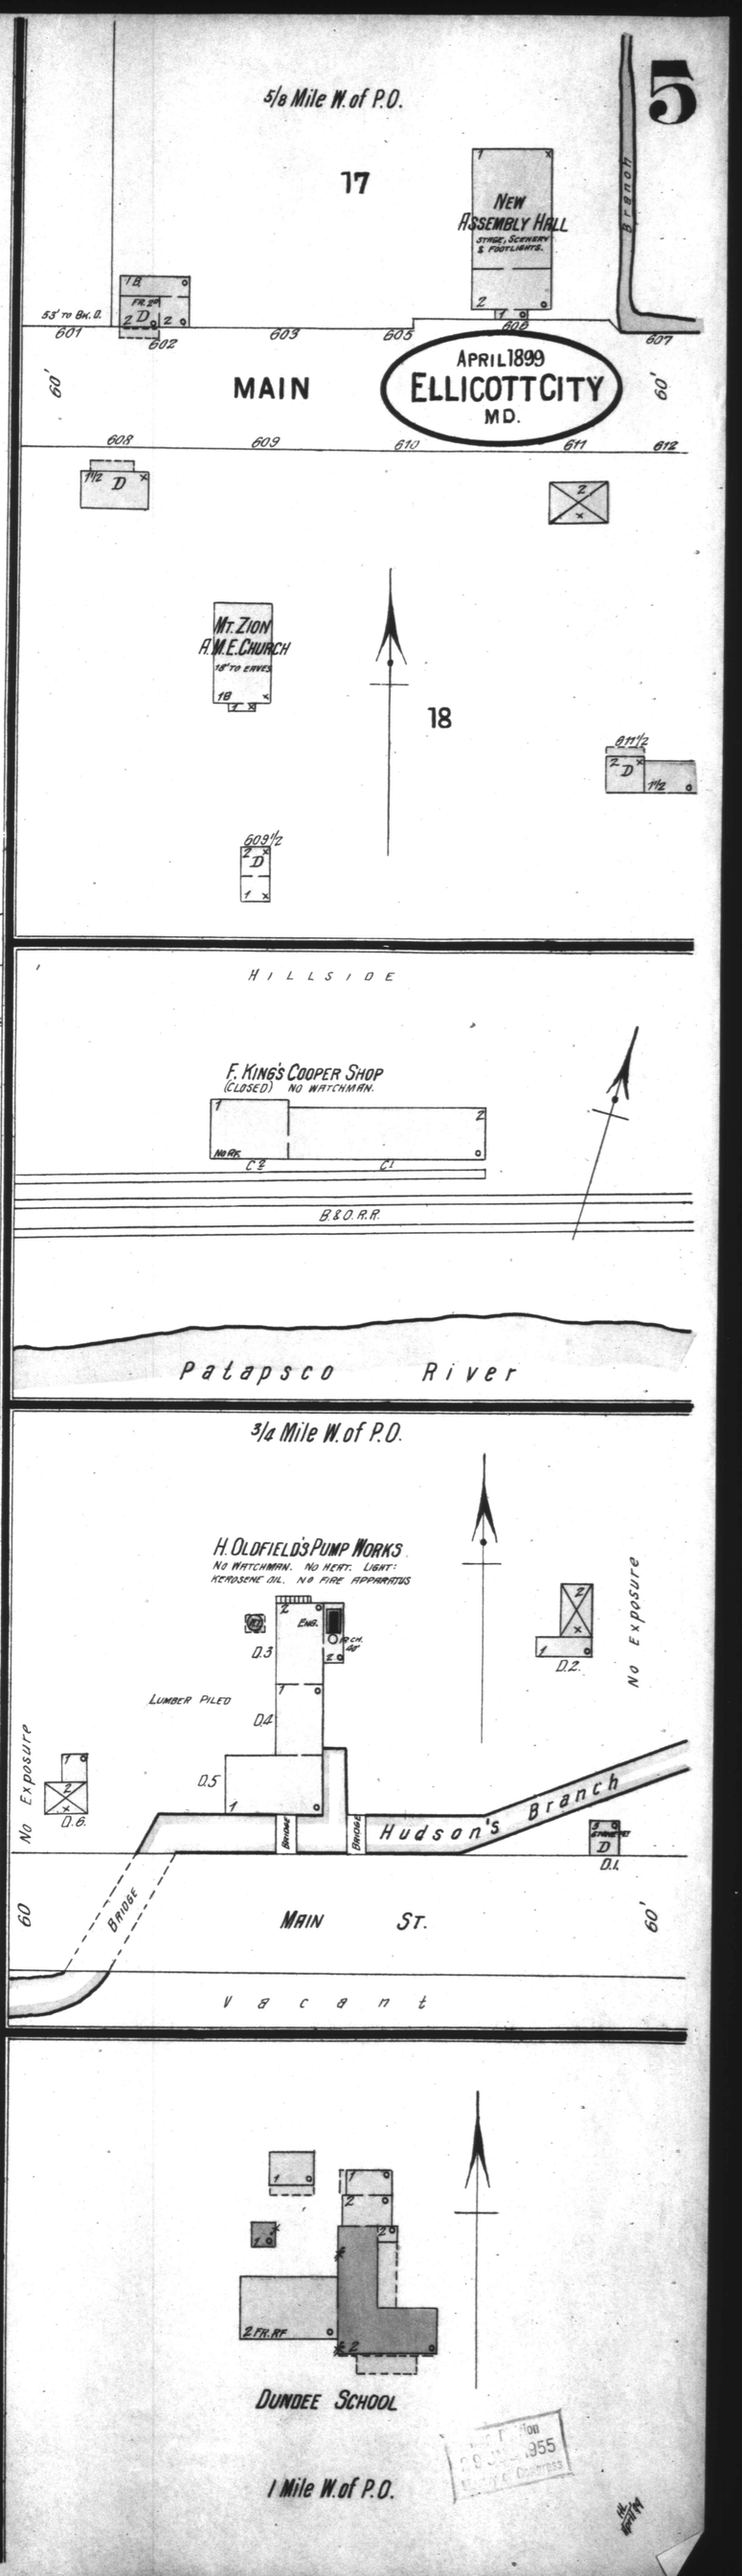
25 SET DOUBLE ROLLS. 1 SET DOUBLE ROLLS (CORN) 7 PURIFIERS. 2 SEPARATORS. 1 COCKLE MACH. 2 BRUSH MACHS. 5 BRANDUSTERS. 33 BOLTING REELS. 72 DUST COLLECTORS. 65 STAND OF ELEVATORS. 1 TO ATTIC. 3 FLOUR PACKERS. 1 CORN ASPIRATOR. CAPY OF CORN PLANT: 95 BARRELS.
