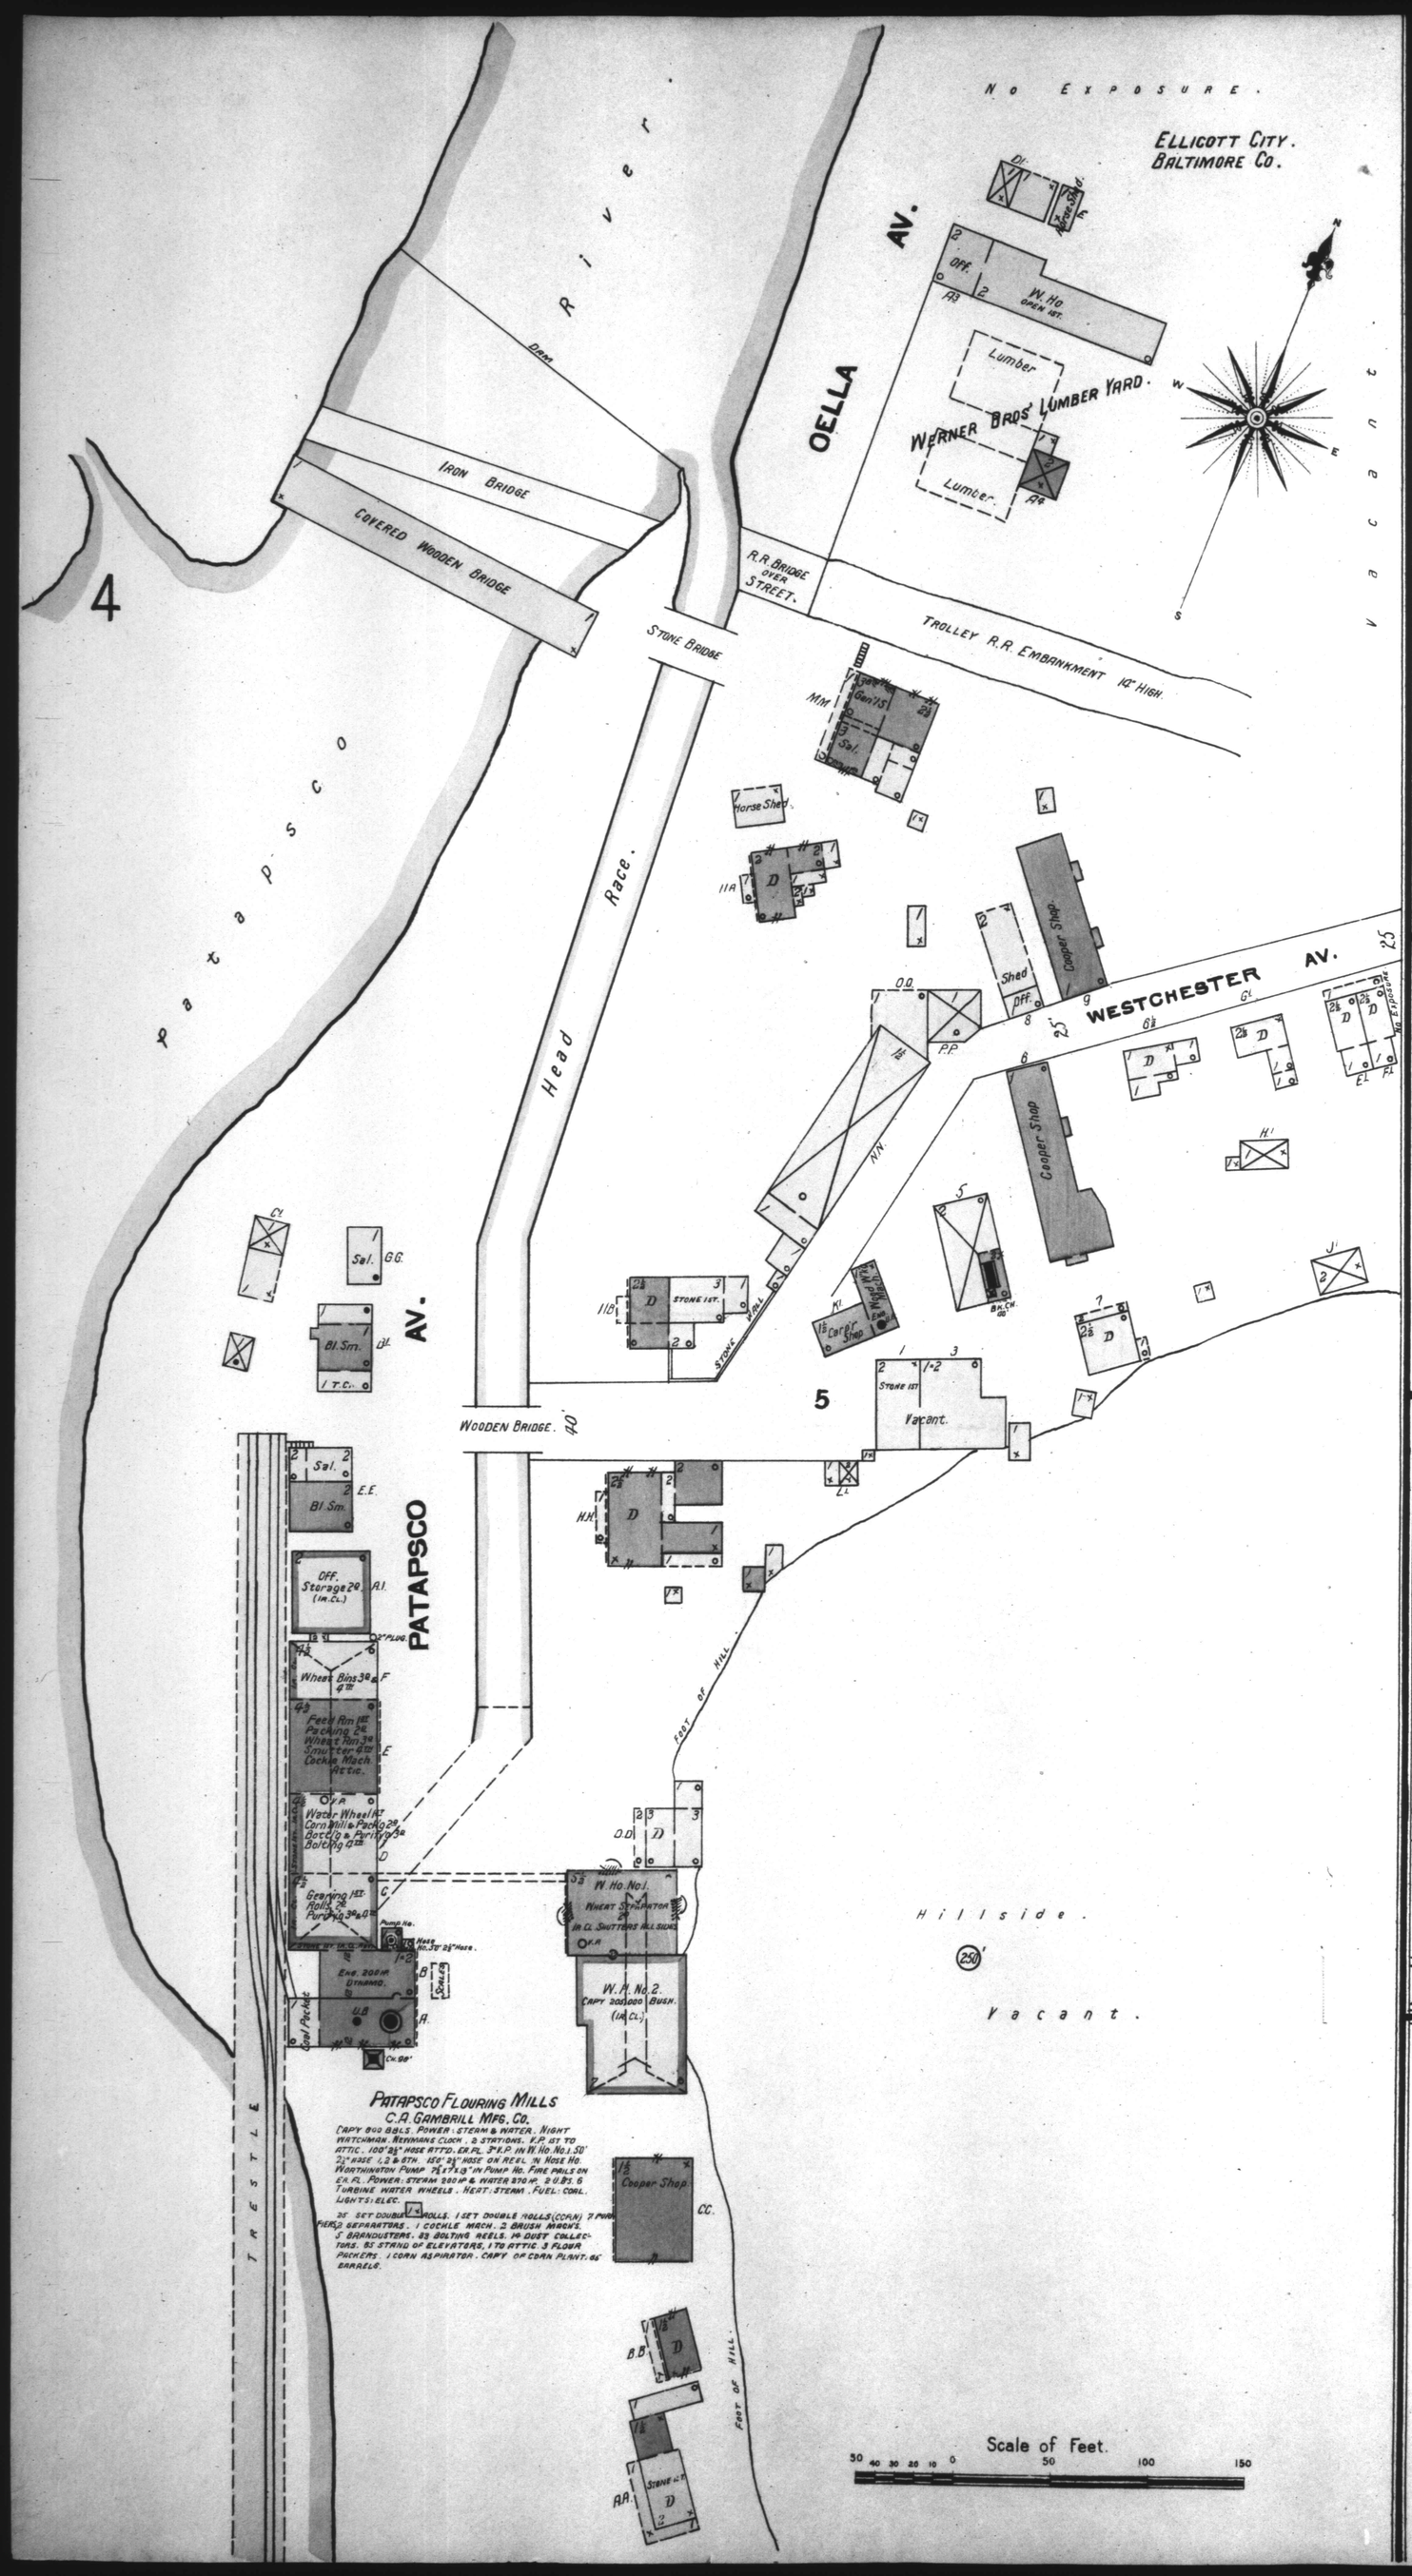
No Exposure.
Ellicott City.
Baltimore Co.
River
Dam
Iron Bridge
Covered Wooden Bridge
4
Stone Bridge
R.R. Bridge over Street.
Trolley R.R. Embankment 12' High.
Oella Av.
Lumber
Werner Bros' Lumber Yard.
Vacant
Head Race.
Patapsco
Horse Shed
Cooper Shop
Shed
Westchester Av.
Stone Wall
Stone 1st
Vacant.
5
Wooden Bridge.
Patapsco Av.
Foot of Hill
Hillside.
Vacant.
Trestle
Patapsco Flouring Mills
C.A. Gambrill Mfg. Co.
Capy 800 Bbls. Power: Steam & Water. Night Watchman. Reinhards Clock. 2 Stations. V.P. at to Attic. 100' 2½" Hose Attd. Er. Fl. 3" V.P. in W. Ho. No. 1. 50' 2½" Hose 1, 2 & 6th. 150' 2½" Hose on Reel in Hose Ho. Worthington Pump 7½" x 7" x 10" in Pump Ho. Fire Rails on Er. Fl. Power: Steam 200 HP & Water 270 HP. 2 O.B.S. 6 Turbine Water Wheels. Heat: Steam. Fuel: Coal. Lights: Elec.
25 Set Double Rolls. 1 Set Double Rolls (Corn) 7 Pairs Separators. 1 Cochle Mach. 2 Brush Mach's. 5 Bran Dusters. 83 Bolting Reels. 14 Dust Collectors. 65 Stand of Elevators, 1 to Attic. 3 Flour Packers. 1 Corn Aspirator. Capy of Corn Plant: 45 Barrels.
Scale of Feet.
50 40 30 20 10 0 50 100 150

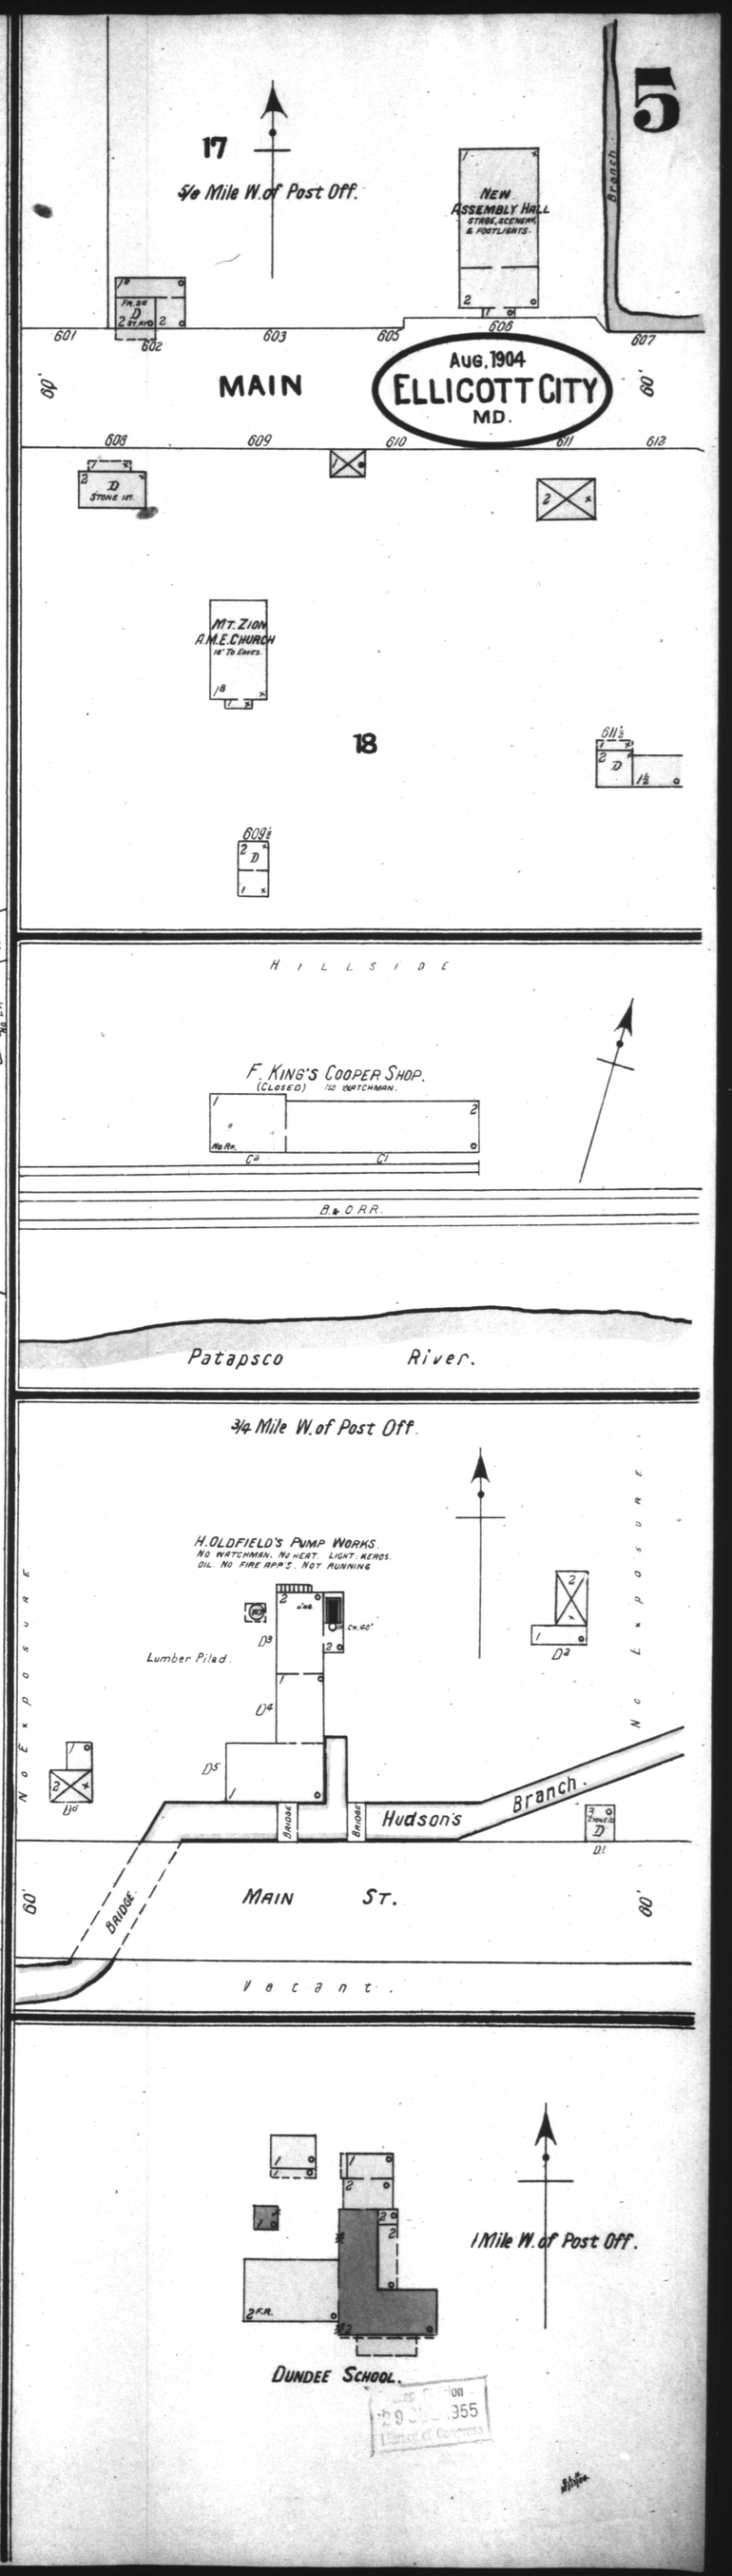
5
17
5/8 Mile W. of Post Off.
New Assembly Hall
Stage, Scenery & Footlights.
Branch
Main
Aug. 1904
Ellicott City
Md.
Mt. Zion A.M.E. Church
18
Hillside
F. King's Cooper Shop.
(Closed)
B. & O. R.R.
Patapsco River.
3/4 Mile W. of Post Off.
H. Oldfield's Pump Works.
No Watchman. No Heat. Light: Keros. Oil. No Fire App's. Not Running
Lumber Piled.
Hudson's Branch.
Main St.
Vacant.
1 Mile W. of Post Off.
Dundee School.
